Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float
Milestones						
C604658ML10	Notice of Award	0	0	01-Oct-10*		10
C604658ML15	Notice to Proceed	0	0	15-Oct-10*		0
C604658ML20	Substantial Completion	0	0		23-Mar-12*	0
C604658ML30	Punchlist	10	10	26-Mar-12	06-Apr-12*	0
C604658ML40	Final Acceptance	0	0		06-Apr-12*	0
Submittals/Procurement						
C604658PR40	Submit - Traffic Signals & Equipment	9	9	09-Feb-11	22-Feb-11	91
C604658PR50	Submit - Storm Water Protection Plan	45	45	10-Feb-11	14-Apr-11	0
C604658PR60	Submit - Health & Safety Plan	5	5	10-Feb-11	16-Feb-11	50
C604658PR10	Submit - Traffic Management Plans	10	10	11-Feb-11	25-Feb-11	44
C604658PR20	Submit - Roadway Materials	5	5	14-Feb-11	18-Feb-11	91
C604658PR62	Reveiw/Approve - Health & Safety Plan	10	10	17-Feb-11	03-Mar-11	50
C604658PR22	Reveiw/Approve - Roadway Materials	10	10	22-Feb-11	07-Mar-11	91
C604658PR42	Review/Approve - Traffic Signals & Equipment	10	10	23-Feb-11	08-Mar-11	91
C604658PR12	Review/Approve - Traffic Management Plans	10	10	28-Feb-11	11-Mar-11	44
C604658PR44	Procure Traffic Signals & Equipment	50	50	09-Mar-11	18-May-11	91
C604658PR52	Reveiw/Approve -Storm Water Protection Plan	20	20	15-Apr-11	13-May-11	0
Mobilization						
C604658MB20	Mobilization	3	3	16-May-11	18-May-11	0
C604658MB25	Install Temp. Signs/Sedimentation Control	3	3	16-May-11	18-May-11	3
Stage 1-NW Foundry Street						
C604658P101	Secure Workzone	1	1	19-May-11	19-May-11	0
C604658P183	Sawcut Roadway	2	2	19-May-11	20-May-11	35
C604658P732	Sawcut Parking Lot	2	2	19-May-11	20-May-11	38
C604658P110	Install Drainage	15	15	20-May-11	10-Jun-11	0
C604658P111	Install Traffic Signal Foundations	10	10	20-May-11	03-Jun-11	80
C604658P120	Excavate for retaining wall	1	1	20-May-11	20-May-11	0
C604658P130	Form/Pour Footing - A	1	1	24-May-11	24-May-11	0
C604658P150	Construct Retaining Wall	19	19	24-May-11	17-Jun-11	0
C604658P115	Relocate Electric/Sprinkler	5	5	25-May-11	31-May-11	13
C604658P140	Form/Pour Footing B	2	2	25-May-11	26-May-11	1
C604658P165	Backfill/Grade at Wall	3	3	20-Jun-11	22-Jun-11	2
C604658P180	Install Granite Curb	10	10	20-Jun-11	01-Jul-11	0
C604658P160	Construct Wood Guard Rail	5	5	23-Jun-11	29-Jun-11	11
C604658P182	Construct Sidewalks & Concrete Drives	14	14	27-Jun-11	15-Jul-11	0
C604658P722	Full Depth Excavation	3	3	13-Jul-11	15-Jul-11	0
C604658P184	Full Depth Pvmt-base/binder	3	3	18-Jul-11	20-Jul-11	0
C604658P712	Temporary Pavement Markings	1	1	20-Jul-11	20-Jul-11	1
Stage 2 - NE Foundry Street						
C604658P201	Secure Work Zone	1	1	13-Jun-11	13-Jun-11	0
C604658P210	Install Drainage	10	10	13-Jun-11	24-Jun-11	0

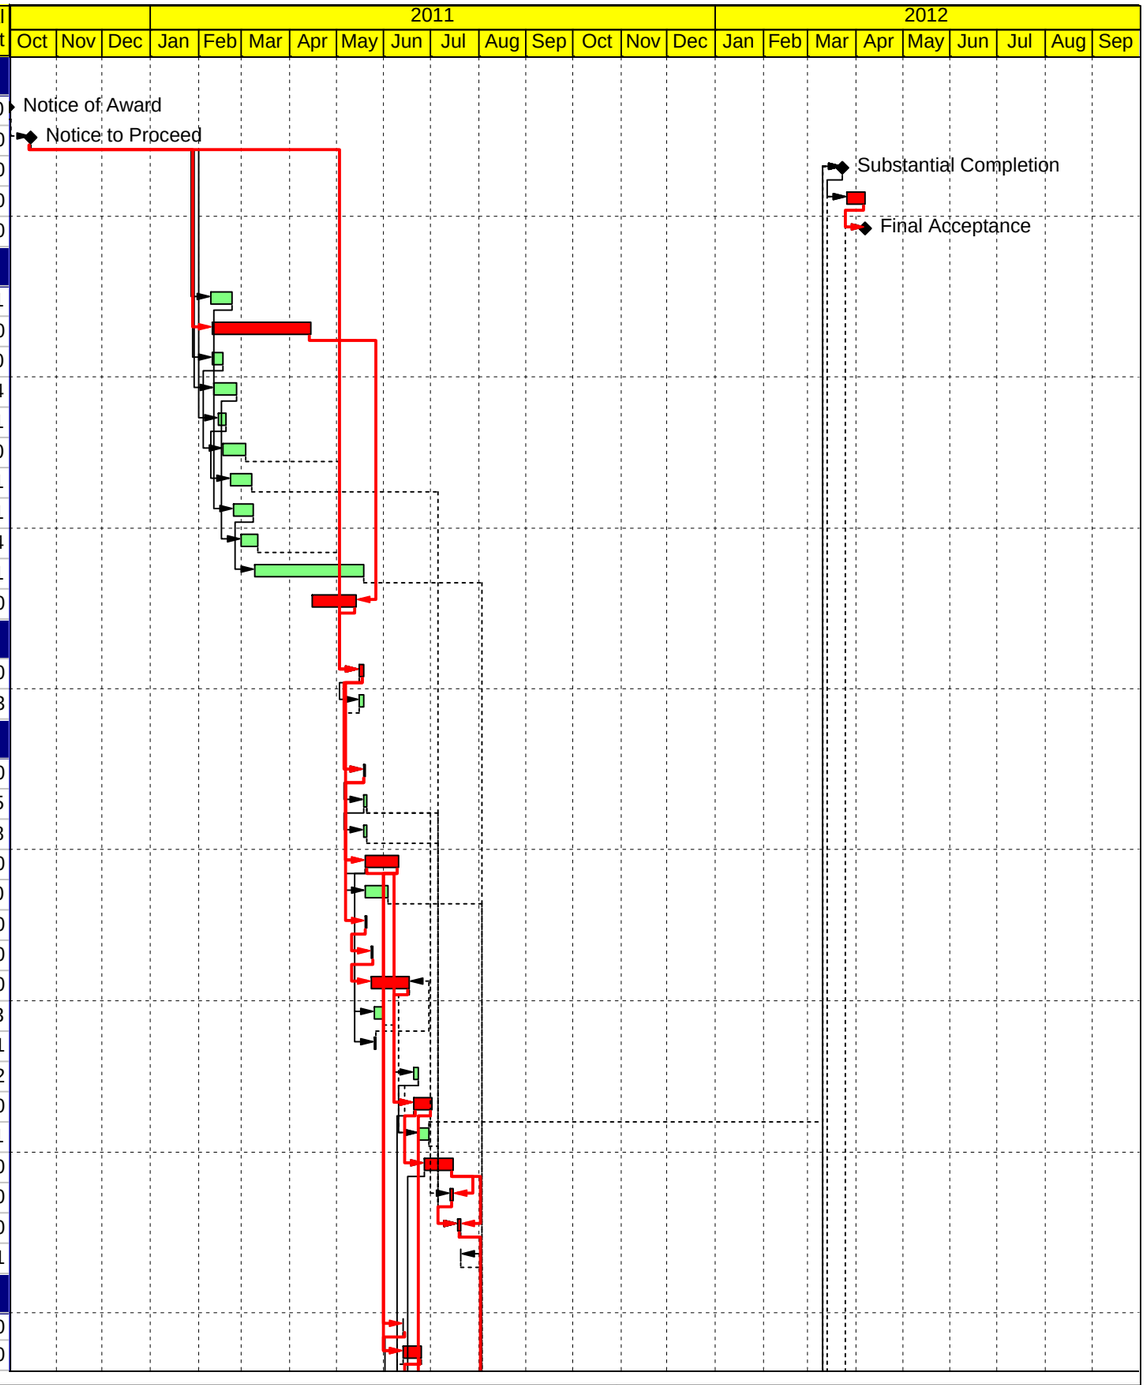

Remaining Level of Effort ◆ Milestone
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

Five Corners Project

Easton, MA

© Primavera Systems, Inc.

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float
C604658P220	Remove Wood Fence	1	1	14-Jun-11	14-Jun-11	10
C604658P230	Remove & Replace Stone Wall	2	2	15-Jun-11	16-Jun-11	10
C604658P240	Remove & Replace Wood Fence	10	10	17-Jun-11	30-Jun-11	10
C604658P280	Install Granite Curb	10	10	22-Jun-11	06-Jul-11	2
C604658P211	Install Traffic Signal Foundations	5	5	27-Jun-11	01-Jul-11	5
C604658P282	Construct Sidewalks & Concrete Drives	15	15	29-Jun-11	20-Jul-11	2
C604658P283	Sawcut Roadway	2	2	05-Jul-11	06-Jul-11	5
C604658P284	Full Depth Excavation	2	2	07-Jul-11	08-Jul-11	5
C604658P275	Full Depth Pvmt - base/binder	3	3	18-Jul-11	20-Jul-11	0
C604658P276	Temporary Pavement Markings	1	1	21-Jul-11	21-Jul-11	0
Stage 3 - SW Foundry Street						
C604658P310	Install Drainage	6	6	27-Jun-11	05-Jul-11	0
C604658P380	Install Granite Curb	12	12	06-Jul-11	21-Jul-11	0
C604658P311	Install Traffic Signal Foundations	5	5	14-Jul-11	20-Jul-11	48
C604658P382	Construct Sidewalks & Concrete Drives	20	20	14-Jul-11	10-Aug-11	8
Stage 4 - SE Foundry Street						
C604658P410	Install Drainage	6	6	06-Jul-11	13-Jul-11	7
C604658P401	Secure Work Zone	1	1	22-Jul-11	22-Jul-11	0
C604658P742	Temporary Pavement Markings	1	1	22-Jul-11	22-Jul-11	0
C604658P480	Install Granite Curb	15	15	25-Jul-11	12-Aug-11	0
C604658P411	Install Traffic Signal Foundations	10	10	01-Aug-11	12-Aug-11	31
C604658P482	Construct Sidewalks & Concrete Drives	20	20	01-Aug-11	26-Aug-11	6
Stage 5 - Depot St./New Bay Road						
C604658P510	Install Drainage	10	10	14-Jul-11	27-Jul-11	13
C604658P515	Relocate Electric	7	7	14-Jul-11	22-Jul-11	16
C604658P501	Secure Work Zone	1	1	15-Aug-11	15-Aug-11	0
C604658P505	R & R Utility Poles (By Others)	2	2	16-Aug-11	17-Aug-11	28
C604658P520	Install Wood Guardrail	5	5	16-Aug-11	22-Aug-11	7
C604658P525	Install New Traffic Signals	10	10	16-Aug-11	29-Aug-11	30
C604658P565	Excavate for Full Depth Pavement	5	5	16-Aug-11	22-Aug-11	0
C604658P511	Install Traffic Signal Foundations	1	1	23-Aug-11	23-Aug-11	24
C604658P530	Modified Rockfill Depot St. at guardrail	15	15	23-Aug-11	13-Sep-11	7
C604658P578	Install Granite Curb for new Bay Road	10	10	23-Aug-11	06-Sep-11	0
C604658P579	Construct Concrete Walk at landscaped area	15	15	07-Sep-11	27-Sep-11	0
C604658P540	Modified Rockfill - Bay Road	15	15	14-Sep-11	04-Oct-11	7
C604658P575	Full Depth Pvmt-base/binder- Bay Road/Depot St.	5	5	28-Sep-11	04-Oct-11	0
C604658P576	Asphalt at driveways	2	2	03-Oct-11	04-Oct-11	0
C604658P582	Reclamation - Entire Project	5	5	05-Oct-11	11-Oct-11	0
C604658P583	Temp Pavement markings	1	1	12-Oct-11	12-Oct-11	1
C604658P584	Activate New Traffic Signals	2	2	12-Oct-11	13-Oct-11	0
C604658P586	New Bay Road Open	1	1	14-Oct-11	14-Oct-11	0
Stage 6 - Bay Road						

Remaining Level of Effort ◆ Milestone
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

Five Corners Project

Easton, MA

© Primavera Systems, Inc.

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float
C604658P610	Install Drainage	10	10	28-Jul-11	10-Aug-11	52
C604658P601	Secure Work Zone	1	1	18-Oct-11	18-Oct-11	0
C604658P630	Excavate monument area	5	5	19-Oct-11	25-Oct-11	0
C604658P680	Install Granite Curb	10	10	26-Oct-11	08-Nov-11	0
C604658P685	Loam & Landscaping	25	25	01-Nov-11	22-Mar-12	1
C604658P682	Construct Concrete Walks & Drives	14	14	02-Nov-11	22-Nov-11	0
C604658P684	Final Paving & Striping - all areas	10	10	09-Nov-11	23-Nov-11	0
C604658P692	Final Finishes/Signage	20	20	09-Nov-11	23-Mar-12	0
C604658P676	Asphalt at driveways	3	3	18-Nov-11	22-Nov-11	11

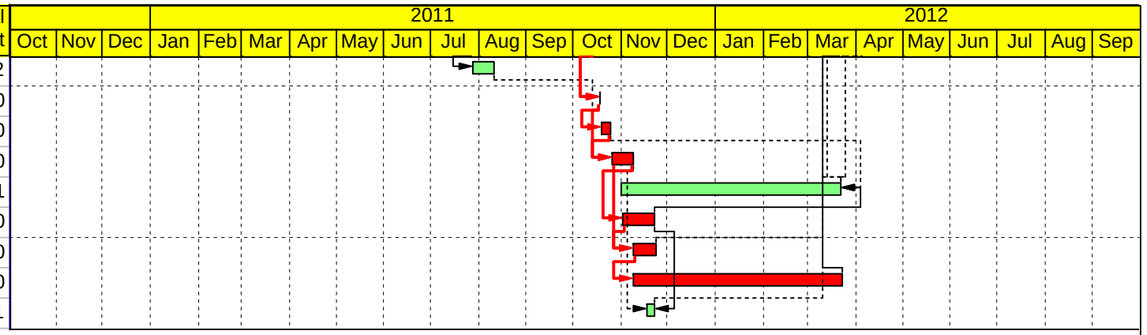

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Five Corners Project

Easton, MA

© Primavera Systems, Inc.
